US Army Corps of Engineers®

Industry Day
Levees and Floodwalls
Acquisition

Tom Podany, Chief, PRO
16 August 2006

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Topics

- Lake Pontchartrain and Vicinity
- West Bank and Vicinity
- New Orleans to Venice
- Larose to Golden Meadow
- Non-Federal Levees
- Grand Isle
- Southeast Louisiana (SELA)

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers

Program

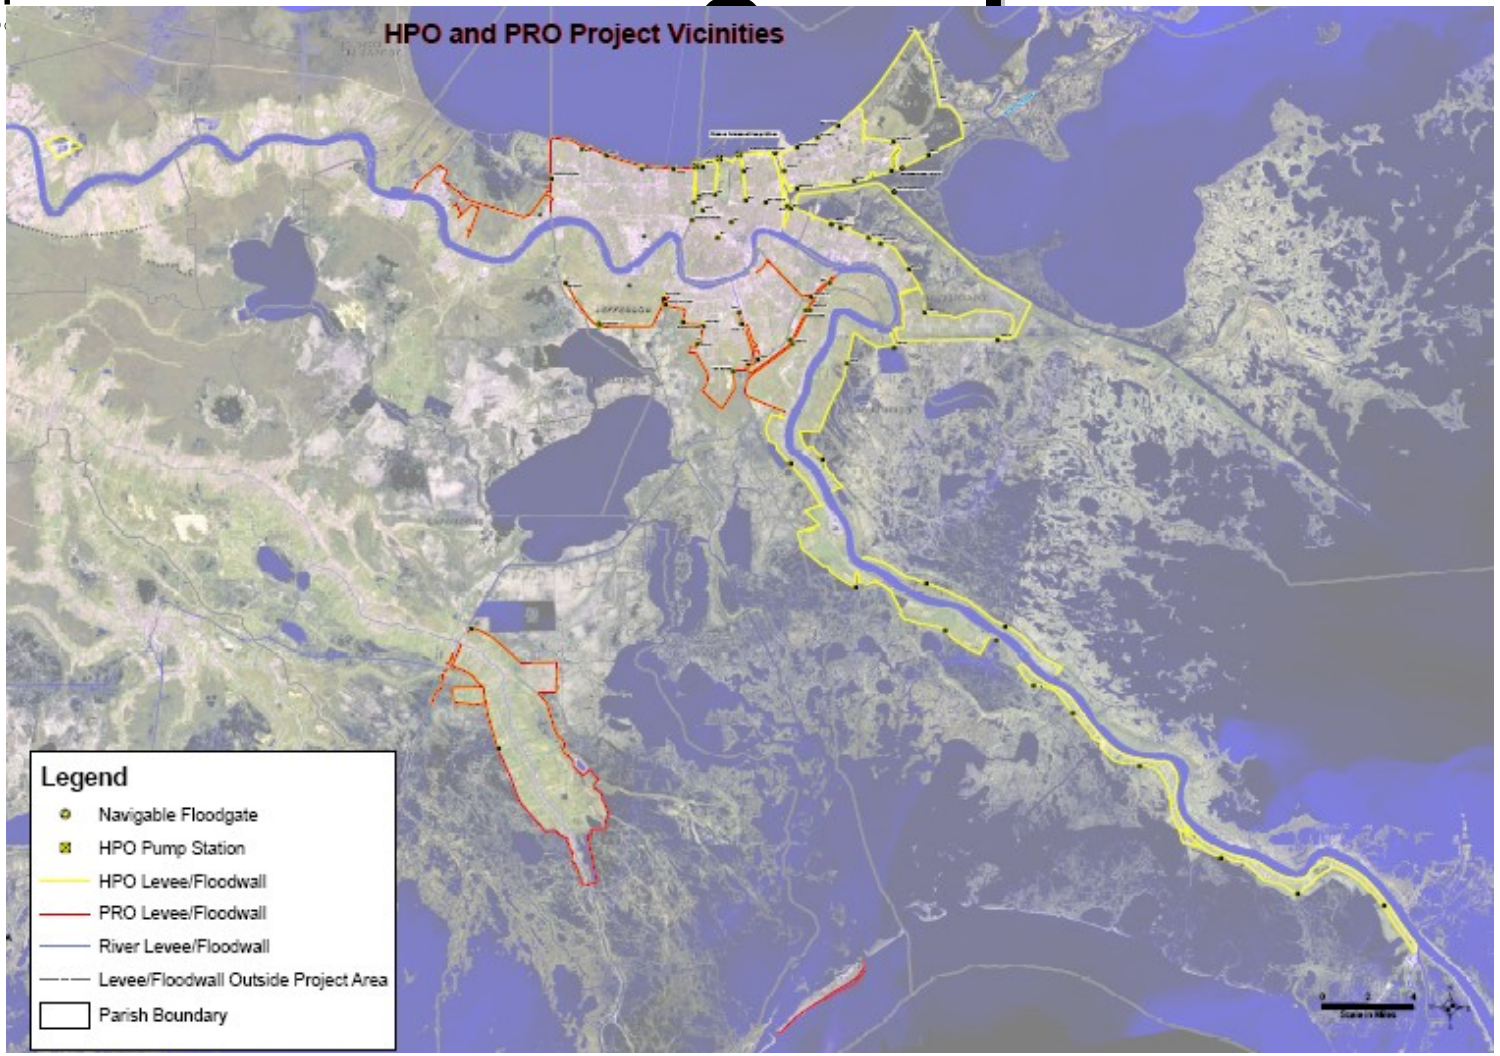

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Recurve I-wall Northwest Kenner

I-310 Floodwall

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Lake Pontchartrain and Vicinity

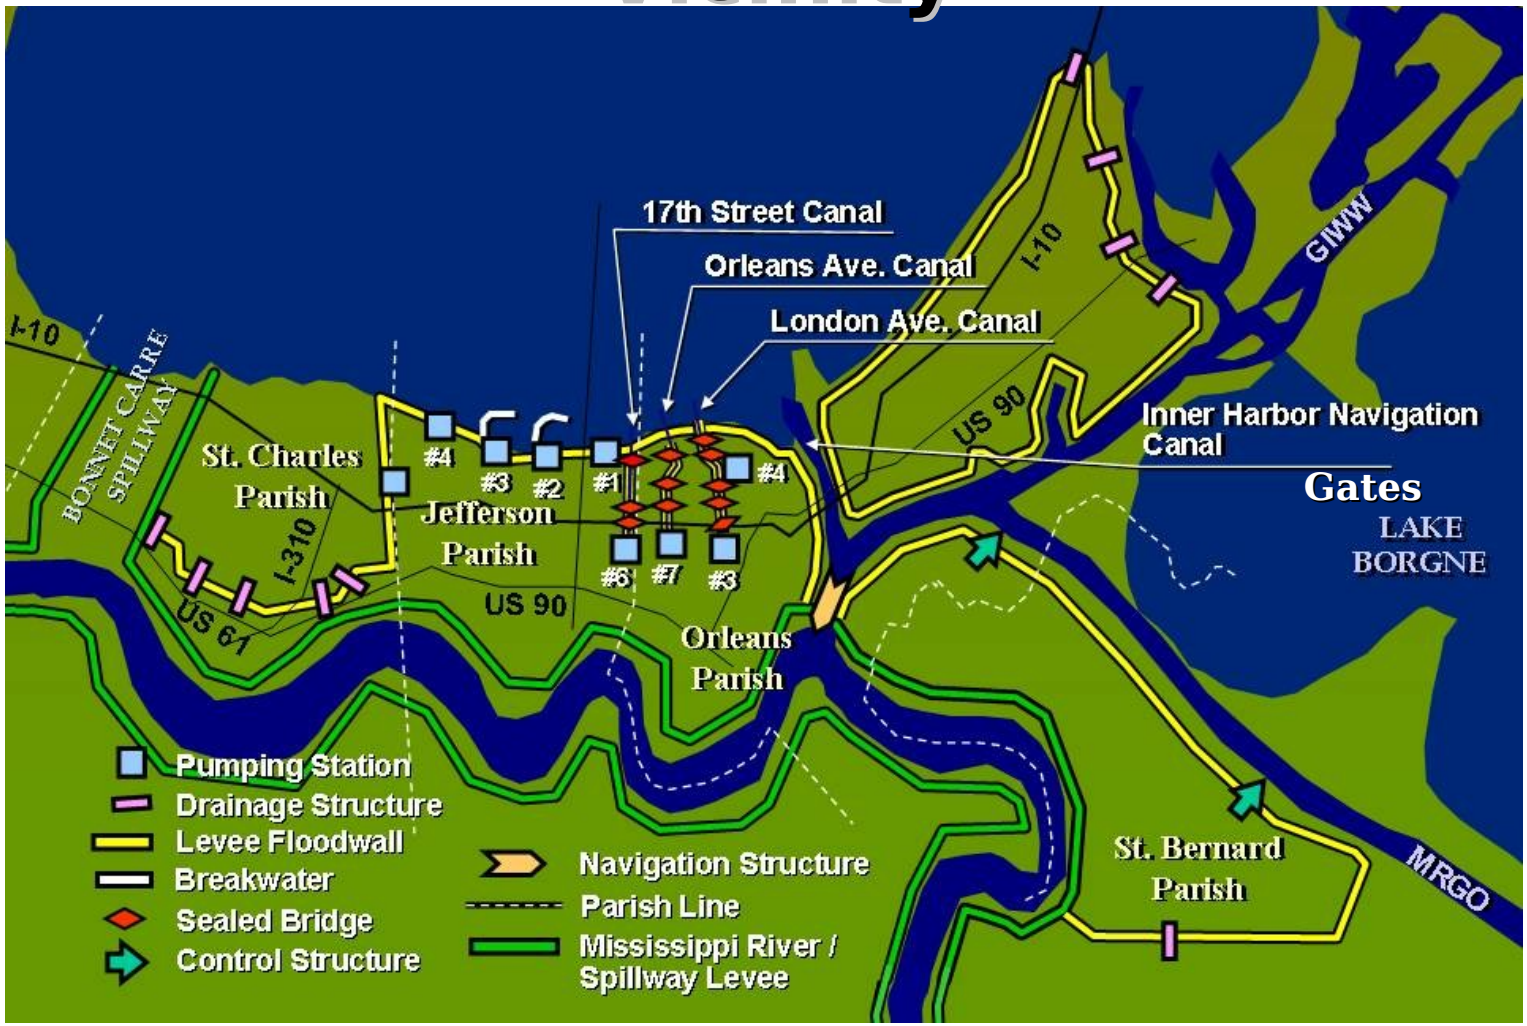

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Lake Pontchartrain and Vicinity

- **Location:** St. Bernard, Orleans, Jefferson and St. Charles Parishes, generally in the vicinity of the city of New Orleans, and between the Mississippi River and Lake Pontchartrain.

- **Purpose:** Hurricane protection for area between Lake Pontchartrain and Miss. River

- **Project Features**
  - Levees
  - Floodwalls

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

Lake Pontchartrain and Vicinity

US Army Corps of Engineers®

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
LPV-00.1	Reach 1 Lakefront Levee- Phase 1	0 to 5M	Q4 2006	8(a)
LPV-00.2	Reach 1 Lakefront Levee- Phase 2	0 to 5M	Q2 2008	8(a)
LPV-01	Reach 2 Lakefront Levee	0 to 5M	Q2 2008	8(a)
LPV-02.1	Reach 3 Lakefront Levee (3rd Lift)- Phase 1	0 to 5M	Q4 2006	8(a)
LPV-02.2	Reach 3 Lakefront Levee- Phase 2	0 to 5M	Q3 2008	8(a)
LPV-03.2	West Return Floodwall - Phase 2	100+M	Q3 2007	Unrestricted
LPV-03a.1	West Return Floodwall - Vintage-Phase 1	0 to 5M	TBD	8(a)
LPV-03b.1	West Return Floodwall, Airport I-wall- Phase 1	0 to 5M	Q3 2006	HUBZONE
LPV-03c.1	West Return Floodwall- I-wall @ I-10- Phase 1	TBD	Q1 2007	HUBZONE
LPV-04.1	Levee - Reach 1A, 1B & 2A- Phase 1	5M to 20M	Q1 2007	Unrestricted - SB Friendly
LPV-04.2	Levee - Reach 1A, 1B & 2A- Phase 2	20M to 50M	Q2 2008	Unrestricted - SB Friendly
LPV-05.1	Levee - Reach 2B (2nd Lift)- Phase 1	0 to 5M	Q4 2006	8(a)
LPV-05.2	Levee - Reach 2B- Phase 2	5M to 20M	Q2 2008	HUBZONE
LPV-06.1	Floodwall Tie-ins- Phase 1	0 to 5M	Q1 2007	Unrestricted
LPV-06a.2	Bonnet Carre Floodwall	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-06b.2	Shell Pipeline Floodwall	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-06c.2	Goodhope Floodwall	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-06d.2	Koch - Gateway Floodwall	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-06e.2	Floodwall Under I-310	5M to 20M	Q3 2007	Unrestricted - SB Friendly
LPV-06f.2	Canadian National Railroad Gate	0 to 5M	Q3 2007	Unrestricted
LPV-07.1	Drainage Structure Tie-ins - Phase 1	5M to 20M	Q1 2007	Unrestricted - SB Friendly
LPV-07a.2	Bayou Trepagnier Drainage Structure - Phase 2	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-07b.2	Cross Bayou Drainage Structure - Phase 2	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-07c.2	St. Rose Drainage Structure - Phase 2	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-07d.2	Almeidia Drainage Structure - Phase 2	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-07e.2	Walker Drainage Structure - Phase 2	0 to 5M	Q3 2007	Unrestricted - SB Friendly
LPV-09.1	Pumping Station #1 (Bonnabel) Floodwall Tie ins- Phase 1	0 to 5M	Q1 2007	HUBZONE
LPV-09.2	Pumping Station #1(Bonnabel) Modification, Fronting Protection, Positiv	5M to 20M	Q3 2007	HUBZONE
LPV-10.1	Pumping Station #2 (Suburban) Floodwall Tie-ins-Phase 1	5M to 20M	Q4 2006	8(a)
LPV-10.2	Pumping Station #2 (Suburban) Modifications, Fronting Protection and F	0 to 5M	Q3 2007	HUBZONE

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

Lake Pontchartrain and Vicinity

US Army Corps of Engineers®

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
LPV-100 A	17th Street Canal Floodwalls	TBD	TBD	HUBZONE
LPV-101	Lakefront Levee OEB - 17th St Canal to Topaz	20M to 50M	Q1 2007	Unrestricted
LPV-102	Lakefront Levee OEB - Topaz to Orleans Canal	5M to 20M	Q1 2007	HUBZONE
LPV-102 A	Orleans Canal Floodwalls	TBD	Q2 2007	TBD
LPV-103	Lakefront Levee OEB - Orleans Canal to London Ave	20M to 50M	Q1 2007	Unrestricted
LPV-103 A	London Ave. Canal Floodwalls	TBD	Q2 2007	TBD
LPV-104	Lakefront Levee OEB - London Avenue Canal to IHNC	20M to 50M	Q1 2007	Unrestricted
LPV-105	Lakefront Airport Floodwalls	100+M	Q1 2007	Unrestricted
LPV-106	Citrus Lakefront Levee (west of Paris Road)	20M to 50M	Q1 2007	Unrestricted - SB Friendly
LPV-107	Lincoln Beach Floodwall	5M to 20M	Q1 2007	HUBZONE
LPV-108	NOE Lakefront Levee	20M to 50M	Q1 2007	Unrestricted - SB Friendly
LPV-109	New Orleans East Levee - South point to CSX RR	20M to 50M	Q2 2007	Unrestricted
LPV-11.1	Pumping Station #3 (Elmwood) Floodwall tie-ins- Phase 1	0 to 5M	Q3 2006	HUBZONE
LPV-11.2	Pumping Station #3 (Elmwood) Modification, Fronting Protection, Positiv	5M to 20M	Q3 2007	HUBZONE
LPV-110	New Orleans East Levee - CSX Railroad Gate	0 to 5M	Q1 2007	8(a)
LPV-111	New Orleans East Back Levee - CSX RR to Michoud Canal	20M to 50M	Q1 2007	Unrestricted
LPV-112	Michoud Canal Floodwall	100+M	Q1 2007	Unrestricted
LPV-113	Citrus Back Levee (Michoud Canal to Michoud Slip) to Auth. Elevation	5M to 20M	Q4 2006	HUBZONE
LPV-114	Michoud Slip	50M To 100M	Q1 2007	Unrestricted
LPV-115	Citrus Back Levee - Michoud Slip to IHNC	20M to 50M	Q1 2007	Unrestricted - SB Friendly
LPV-116	Eastbank IHNC - GIWW/MRGO to Almonaster	5M to 20M	Q1 2007	8(a)
LPV-117	Eastbank IHNC - Almonaster to Lakefront Floodwall	50M To 100M	Q1 2007	Unrestricted
LPV-118	Westbank IHNC - IHNC Lock to Florida Ave.	50M To 100M	Q1 2007	Unrestricted
LPV-119	Westbank IHNC - Florida Ave to Almonaster	50M To 100M	Q1 2007	Unrestricted
LPV-12.1	Pumping Station #4 (Duncan) Floodwall Tie-ins- Phase 1	0 to 5M	Q1 2007	HUBZONE
LPV-12.2	Pumping Station #4 (Duncan) Modification, Fronting Protection, Positive	5M to 20M	Q3 2007	HUBZONE
LPV-120	Westbank IHNC - Almonaster to Lakefront Floodwall	50M To 100M	Q1 2007	Unrestricted
LPV-121	Eastbank IHNC - IHNC Lock to Florida Ave	5M to 20M	Q1 2007	HUBZONE
LPV-13.1	Re-Curve I-Wall in Northwest Kenner- Phase 1	0 to 5M	Q1 2007	HUBZONE
LPV-13.2	Re-Curve I-Wall in Northwest Kenner- Phase 2	20M to 50M	Q3 2007	HUBZONE

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

Lake Pontchartrain and Vicinity

US Army Corps of Engineers®

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
LPV-141	Chalmette Loop Levee - Florida Ave to 50+00.	5M to 20M	Q1 2007	Unrestricted - SB Friendly
LPV-142	Chalmette Loop Levee - 50+00 to Paris Road.	20M to 50M	Q1 2007	Unrestricted - SB Friendly
LPV-143	Chalmette Loop Levee - Paris Road to Bayou Bienvenue	5M to 20M	Q1 2007	HUBZONE
LPV-144	Chalmette Loop Levee - Bayou Bienvenue and Bayou Dupre Floodgates	50M To 100M	Q1 2007	Unrestricted
LPV-145	Chalmette Loop Levee - Bayou Bienvenue to Bayou Dupre.	5M to 20M	Q1 2007	HUBZONE
LPV-146	Chalmette Loop Levee - Bayou Dupre to Hwy 46	5M to 20M	Q1 2007	HUBZONE
LPV-147	Chalmette Loop Levee - Bayou Road Floodgate	0 to 5M	Q1 2007	8(a)
LPV-148	Chalmette Loop Levee - Hwy 46 to River (Verret to Caernarvon) - raise	50M To 100M	Q1 2007	Unrestricted
LPV-149	Chalmette Loop Levee - Verret to Caernarvon Structures - Concept Stu	50M To 100M	Q1 2007	Unrestricted
LPV-16.1	Floodwall and Gate at Bonnabel Boat Launch- Phase 1	0 to 5M	Q1 2007	HUBZONE
LPV-16.2	Floodwall and Gate at Bonnabel Boat Launch- Phase 2	5M to 20M	Q3 2007	Unrestricted
LPV-17.1	Bridge Abutment and Floodwall tie-ins at Causeway Bridge - Phase 1	0 to 5M	Q1 2007	HUBZONE
LPV-17.2	Bridge abutment and Floodwall Tie-ins at Causeway Bridge -Phase 2	20M to 50M	Q3 2007	HUBZONE
LPV-18.1	Floodwall and Gate at Williams Blvd. Boat Launch - Phase 1	0 to 5M	Q1 2007	HUBZONE
LPV-18.2	Floodwall and Gate at Williams Blvd. Boat Launch-Phase 2	5M to 20M	Q3 2007	HUBZONE
LPV-201	IHNC levee repairs	0 to 5M	Q1 2007	8(a)
LPV-202	IHNC floodwall repairs	0 to 5M	Q1 2007	8(a)
LPV-34	Backflow prevention- sluice gates @ PS #1, #2, #3, and #4- Phase 1	0 to 5M	Q1 2007	HUBZONE

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

West Bank and Vicinity

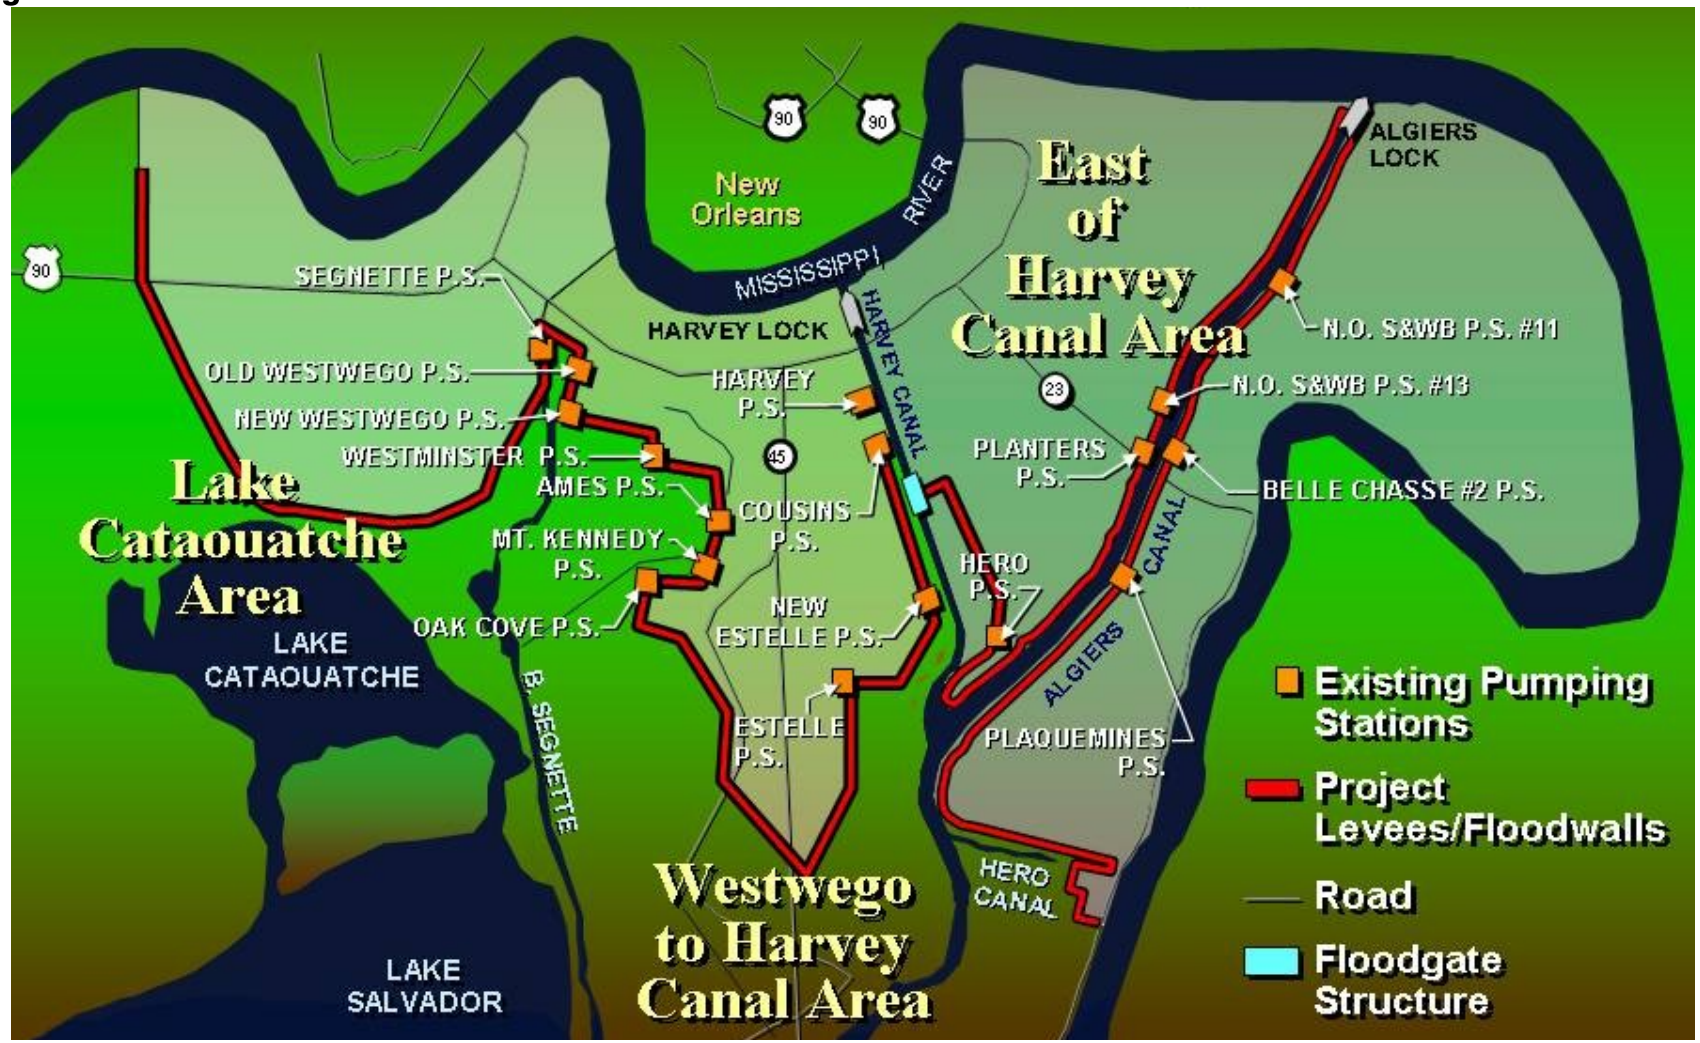

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers

West Bank and Vicinity

- **Location:** West bank of the Mississippi River in the vicinity of New Orleans; in Jefferson, Orleans and Plaquemines parishes.
- **Purpose:** Hurricane protection from surges in Lakes Cataocuatche and Salvador, and waterways leading to the Gulf of Mexico.
- **Project Features**
  - Westwego to Harvey (East and West of Algiers Canal)
    - 22 miles of earthen levee and 2 miles of floodwalls
      - Levees/Floodwalls
  - Lake Cataouatche Area
    - 10 miles of levee and 2 miles of floodwalls
  - East of Harvey Canal
    - 25 miles of levee and 5 miles of floodwalls, includes a sector floodgate in the Harvey Canal just below Lapalco Boulevard

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

West Bank and Vicinity

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
WBV-01	Contract 1, Sectorgate to Boomtown Floodwall	50M To 100M	Q1 2007	Unrestricted
WBV-02a	Contract 2a, Boomtown to Hero PS Floodwalls	50M To 100M	Q1 2007	Unrestricted
WBV-02b	Contract 2b, Boomtown to Hero PS Floodwalls	5M to 20M	Q1 2007	Unrestricted
WBV-03a	Contract 3a, Hero PS to Algiers Canal Floodwall	20M to 50M	Q4 2006	Unrestricted
WBV-03b	Contract 3b, Hero PS to Algiers Canal Floodwall	20M to 50M	Q1 2007	Unrestricted
WBV-04.1	Belle Chasse Hwy to Hero Cutoff-Reach 1-Phase 1	0 to 5M	Q1 2007	HUBZONE
WBV-04.2	Belle Chasse Hwy to Hero Cutoff-Reach1-Phase 2	5M to 20M	Q3 2008	HUBZONE
WBV-05.1	Belle Chasse Hwy to Hero Cutoff-Reach 2-Phase 1	0 to 5M	Q1 2007	HUBZONE
WBV-05.2	Belle Chasse Hwy to Hero Cutoff-Reach 2-Phase 2	5M to 20M	Q3 2008	HUBZONE
WBV-06.1	Belle Chasse Hwy to Hero Cutoff-Reach 3 & 4-phase 1	5M to 20M	Q1 2007	HUBZONE
WBV-06.2	Belle Chasse Hwy to Hero Cutoff-Reach 3 & 4-Phase 2	5M to 20M	Q3 2008	HUBZONE
WBV-07	Planters PS Fronting Protection and Modifications	20M to 50M	Q1 2007	HUBZONE
WBV-08	S&WB PS #13 Fronting Protection and Modifications	5M to 20M	Q1 2007	HUBZONE
WBV-09.1	Hero Canal to Oakville- Phase 1	0 to 5M	Q4 2007	HUBZONE
WBV-09.2	Hero Canal to Oakville- Phase 2	TBD	Q3 2008	HUBZONE
WBV-10	Belle Chasse PS #1 (Plaquemines PS) Fronting Protection and Modifica	20M to 50M	Q1 2007	Unrestricted - SB Friendly
WBV-11	Belle Chasse PS #2 Fronting Protection and Modifications	20M to 50M	Q1 2007	Unrestricted - SB Friendly
WBV-12.1	Hero Canal Reach 1, 2nd Enlgt-Phase 1	0 to 5M	Q1 2007	8(a)
WBV-12.2	Hero Canal-Reach 1-Phase 2	TBD	Q3 2008	Unrestricted
WBV-13	S&WB PS #11Fronting Protection and Modifications	20M to 50M	Q1 2007	HUBZONE
WBV-14a.1	Estelle PS to Vicinity of Lapalco Overpass, 2nd Englt Phase 1	0 to 5M	Q1 2007	HUBZONE
WBV-14a.2	Estelle PS to Vicinity of Lapalco Overpass- Phase 2	5M to 20M	Q3 2008	HUBZONE
WBV-14b.1	Orleans Village to Hwy 45, Levee-Phase 1	0 to 5M	Q1 2007	8(a)
WBV-14b.2	Orleans Village to Hwy 45 Levee- Phase 2	5M to 20M	Q3 2008	HUBZONE
WBV-14c.1	New Westwego PS to Orleans Village, 3rd Enlgt-Phase 1	0 to 5M	Q1 2007	8(a)
WBV-14c.2	New Westwego PS to Orleans Village- Phase 2	5M to 20M	Q3 2008	HUBZONE
WBV-14d	V-line Floodwall	TBD	Q1 2008	HUBZONE
WBV-14e.1	V-line Levee, east of Vertex- Phase 1	5M to 20M	Q1 2007	HUBZONE
WBV-14e.2	V-line levee, east of vertex- Phase 2	5M to 20M	Q3 2008	HUBZONE
WBV-14f.1	Hwy 45 levee, 2nd Enlgt - Phase 1	0 to 5M	Q1 2007	HUBZONE
WBV-14f.2	Hwy 45 levee- Phase 2	0 to 5M	Q3 2008	HUBZONE

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

West Bank and Vicinity

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
WBV-15a.1	Lake Cataouatche PS to Segnette State Park-Phase 1	5M to 20M	Q1 2007	HUBZONE
WBV-15a.2	Lake Cataouatche PS to Segnette State Park-Phase 2	TBD	Q1 2008	HUBZONE
WBV-15b	Lake Cataouatche PS Fronting Protection, Modifications	TBD	Q2 2007	Unrestricted
WBV-16	Segnette PS to Company Canal and Company Canal Floodwall	20M to 50M	Q4 2007	Unrestricted - SB Friendly
WBV-17a.1	Western Tie-In-Phase 1	0 to 5M	Q3 2007	HUBZONE
WBV-17a.2	Western Tie-In- Phase 2	5M to 20M	Q1 2009	HUBZONE
WBV-17b.1	Station 160+00 to Hwy 90- Phase 1	TBD	Q2 2007	HUBZONE
WBV-17b.2	Station 160+00 to Hwy 90- Phase 2	TBD	Q3 2008	HUBZONE
WBV-18.1	Hwy 90 to Lake Cataouatche PS - Phase 1	5M to 20M	Q4 2006	Unrestricted - SB Friendly
WBV-18.2	Hwy 90 to Lake Cataouatche PS - Phase 2	5M to 20M	Q3 2008	Unrestricted - SB Friendly
WBV-20	New Westwego PS fronting Protection and Modifications	TBD	Q2 2007	Unrestricted - SB Friendly
WBV-21	Old Westwego PS Fronting Protection and Modifications	0 to 5M	Q2 2007	Unrestricted - SB Friendly
WBV-22	Old to New Westwego Floodwall	20M to 50M	Q4 2007	Unrestricted - SB Friendly
WBV-23	New Estelle PS Fronting Protection and Modifications	TBD	Q3 2007	HUBZONE
WBV-24	Segnette State Park Floodwall	TBD	Q4 2007	HUBZONE
WBV-30	Westminster PS Fronting Protection and Modifications	TBD	Q2 2007	Unrestricted - SB Friendly
WBV-33	Old Estelle PS Fronting Protection and Modifications	TBD	Q3 2007	HUBZONE
WBV-37	Ames PS fronting Protection and Modifications	TBD	Q2 2007	8(a)
WBV-38.1	Cousins PS- Phase 1	TBD	TBD	Unrestricted - SB Friendly
WBV-38.2	Cousins PS- Phase 2	TBD	Q4 2007	Unrestricted - SB Friendly
WBV-39	Cousins Discharge Channel	TBD	Q2 2007	TBD
WBV-43	Mt. Kennedy PS fronting protection and Modifications	TBD	Q2 2007	8(a)
WBV-44	Whitney Barataria PS Fronting Protection and Modifications	TBD	Q3 2007	HUBZONE
WBV-46.2	Sector gate complex- Phase 2	TBD	Q4 2007	TBD
WBV-47	Algiers Lock to Belle Chasse Hwy (West)- Phase 2	TBD	Q3 2008	TBD
WBV-48.1	Belle Chasse Hwy to Algiers Lock (East) - Phase 1	TBD	TBD	TBD
WBV-48.2	Belle Chase Hwy to Algiers Lock (East)- Phase 2	TBD	Q3 2008	TBD
WBV-49	Hero Levee to Belle Chasse Hwy (East)- Phase 2	TBD	Q3 2008	TBD
WBV-52	Priority Interim-Contract 1	0 to 5M	Q4 2006	8(a)
WBV-53	Priority Interim-Contract 2	0 to 5M	Q4 2006	8(a)
WBV-54	Priority Interim- Contract 3	0 to 5M	Q4 2006	8(a)
WBV-55	Priority Interim- Contract 4	0 to 5M	Q4 2006	8(a)
WBV-56	Priority Interim-Contract 5	0 to 5M	TBD	8(a)
WBV-57	Interim Back Flow Prevention	0 to 5M	Q1 2007	TBD

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

New Orleans to Venice

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

New Orleans to Venice

- **Location**: Along the east bank of the Miss. River from Phoenix, Louisiana down to Bohemia, LA and along the west river bank from St. Jude to the vicinity of Venice
- **Purpose**: Provide hurricane protection in the Mississippi River delta region.
- **Project Features**: About 87 miles of river and back levees and 13 flap-gated culverts.

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

New Orleans to Venice

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
NOV-01	Reach C Hurricane Protection	20M to 50M	Q1 2007	Unrestricted
NOV-02	Reach C Hurricane Protection	20M to 50M	Q1 2007	Unrestricted - SB Friendly
NOV-03	East Bank MRL Reach 1	TBD	Q1 2007	8(a)
NOV-04	East Bank MRL Reach 2	TBD	Q1 2007	8(a)
NOV-05	St. Jude - City Price Upper Reach A	20M to 50M	Q1 2007	Unrestricted - SB Friendly
NOV-06	Reach A (City Price to Empire)	0 to 5M	Q1 2007	8(a)
NOV-07	Reach B-1 (Empire to Ft Jackson)	5M to 20M	Q1 2007	HUBZONE
NOV-08	Reach B-2 (Ft. Jackson to Venice)	5M to 20M	Q1 2007	8(a)
NOV-09	West Bank MRL	5M to 20M	Q2 2007	8(a)
NOV-10	West Bank MRL - St Jude to Port Sulphur	20M to 50M	Q1 2007	Unrestricted - SB Friendly
NOV-11	West Bank MRL - Port Sulphur to Fort Jackson Sta 285 to 357 Buras to	50M To 100M	Q1 2007	Unrestricted
NOV-12	West Bank MRL - Fort Jackson to Venice	50M To 100M	Q1 2007	Unrestricted
NOV-13	Empire Floodgate	50M To 100M	Q1 2007	Unrestricted
NOV-14	Empire Lock	50M To 100M	Q1 2007	Unrestricted
NOV-15	Floodwall Repairs Duuic P/S, GrandLaird P/S, Pt Michel, Childress	0 to 5M	Q1 2007	HUBZONE

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Larose to Golden Meadow

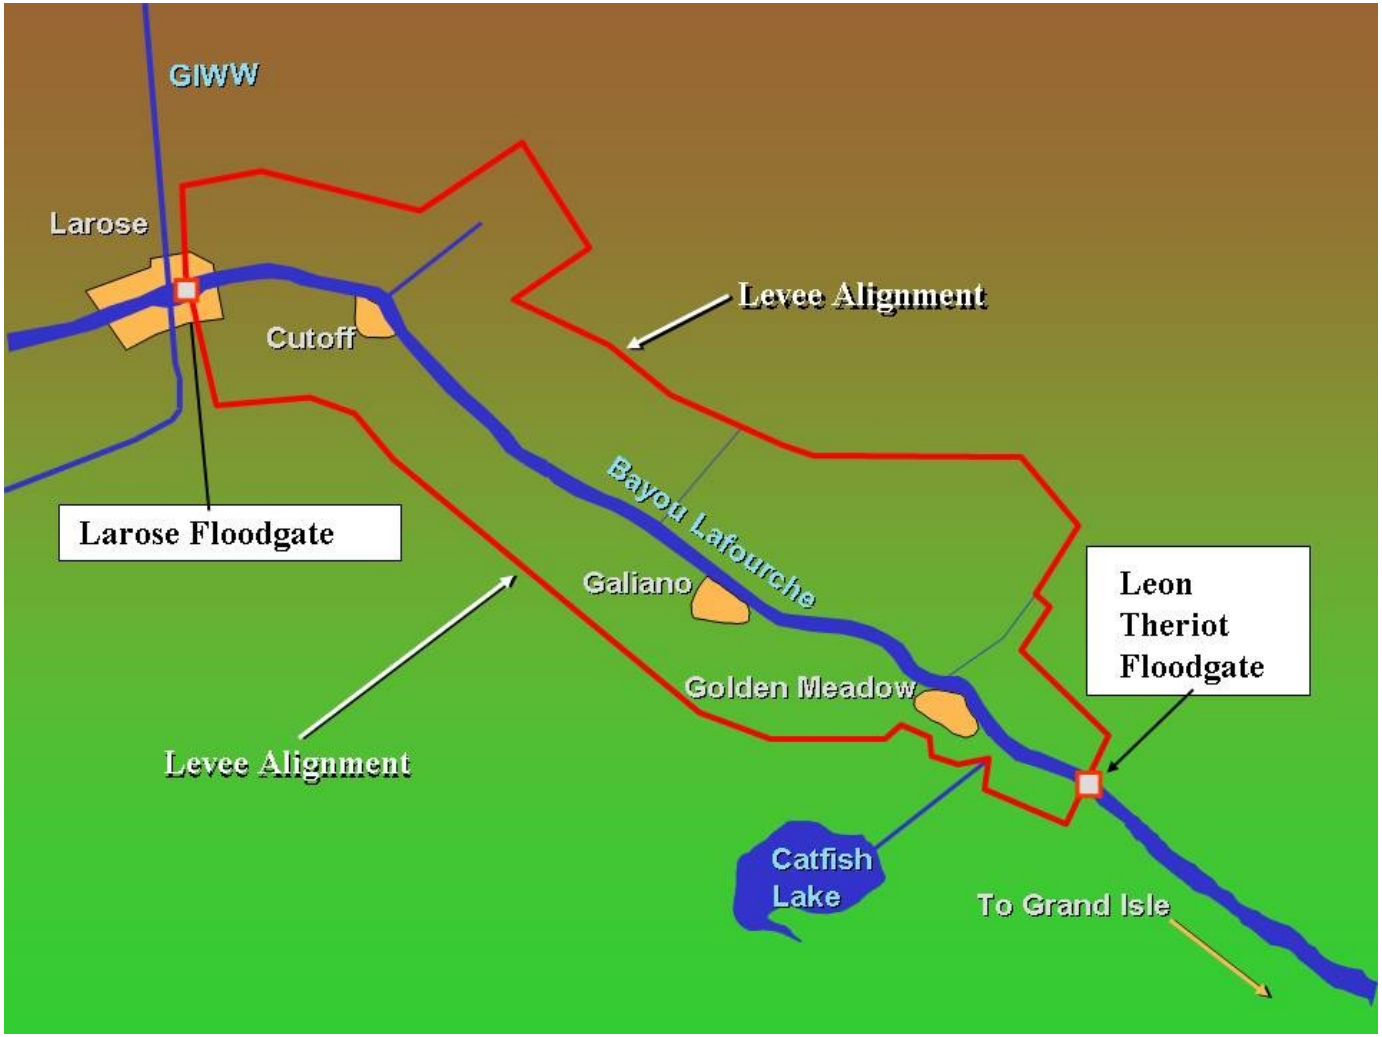

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Larose to Golden Meadow

- **Location:** Lafourche Parish about 50 miles south of New Orleans along Bayou Lafourche between Larose and Golden Meadow.
- **Purpose:** Provide protection to the communities located along Bayou Lafourche between Larose and Golden Meadow.
- **Project Features:** Ring levee about 40 miles in length.
  - Levees
  - Floodwalls

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Larose to Golden Meadow

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
LGM-00	Section D: South Berm and Mitigation Levee	0 to 5M	Q1 2007	8(a)
LGM-01	C North 3rd Lift	0 to 5M	Q2 2007	8(a)
LGM-02	D North 3rd Lift	0 to 5M	Q4 2006	8(a)

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Non Federal Levees

- **Location:** Grand Isle and Plaquemines Parish
- **Purpose:** Bring Non-Federal levees into Federal system
- **Project Features:** Levees

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
NF-01	Grand Isle Non Federal	5M to 20M	Q2 2007	8(a)
NF-02	Braithwaite to Scarsdale Non Federal	5M to 20M	Q2 2007	Unrestricted
NF-03	Plaquemines Eastbank Non Federal	20M to 50M	Q2 2007	HUBZONE
NF-04	Plaquemines Westbank Non Federal	20M to 50M	Q1 2007	8(a)
NF-05	Oakville to St. Jude	50M To 100M	Q4 2007	Unrestricted
NF-06	Oakville to St. Jude	50M To 100M	Q4 2007	8(a)

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Grand Isle

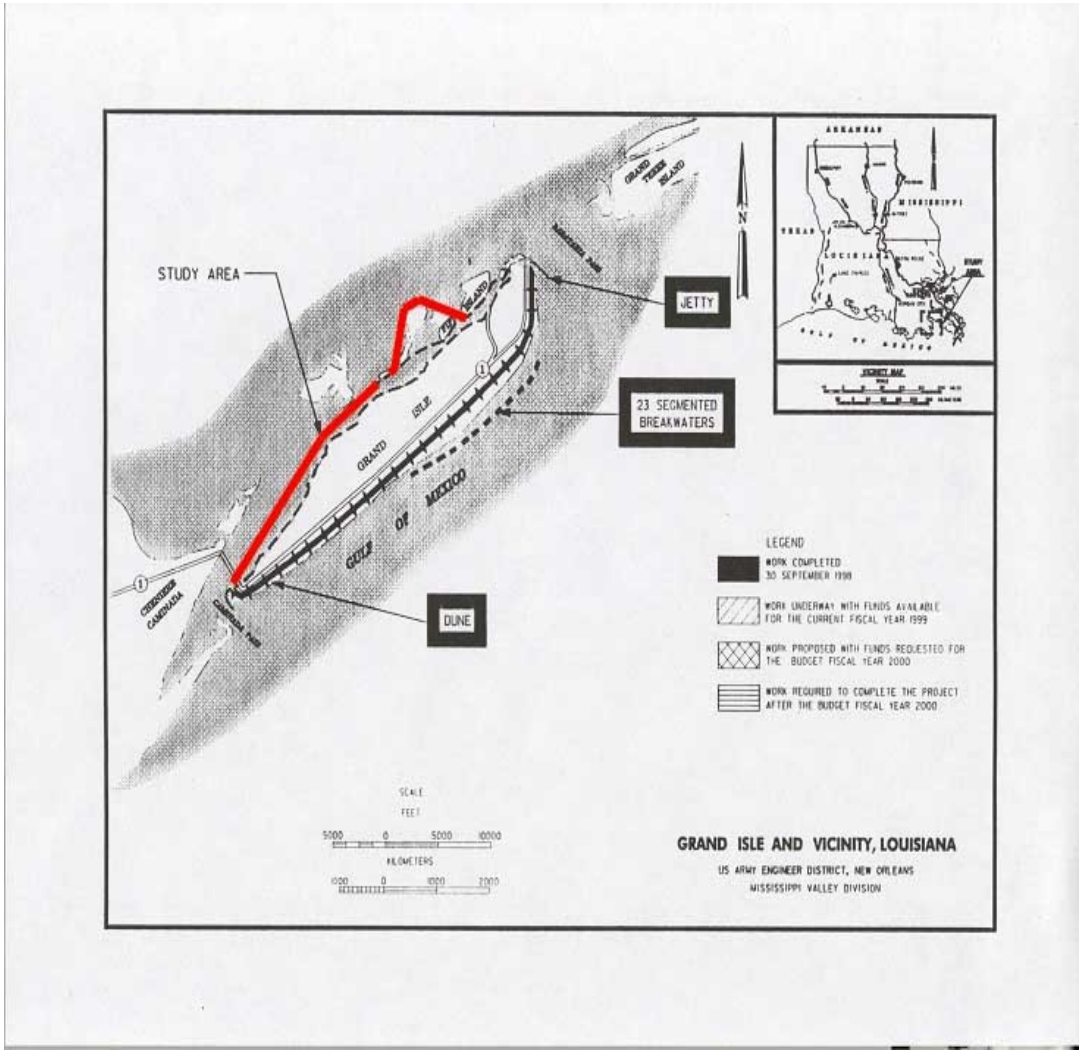
STUDY AREA
JETTY
23 SEGMENTED BREAKWATERS
DUNE
GULF OF MEXICO
GRAND ISLE
LEGEND
WORK COMPLETED 30 SEPTEMBER 1998
WORK UNDERWAY WITH FUNDS AVAILABLE FOR THE CURRENT FISCAL YEAR 1999
WORK PROPOSED WITH FUNDS REQUESTED FOR THE BUDGET FISCAL YEAR 2000
WORK REQUIRED TO COMPLETE THE PROJECT AFTER THE BUDGET FISCAL YEAR 2000
SCALE
FEET
KILOMETERS
GRAND ISLE AND VICINITY, LOUISIANA
US ARMY ENGINEER DISTRICT, NEW ORLEANS
MISSISSIPPI VALLEY DIVISION

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Grand Isle

➢**PROJECT LOCATION:** The proposed work is located on the gulf coast of southern Jefferson Parish. It is about 50 miles south of New Orleans and 45 miles northwest of the mouth of the Mississippi River.

➢**PROJECT PURPOSE:** The project provides for flood control and coastal protection on the Island.

➢**PROJECT FEATURES:** Levee system

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
GI-01	Grand Isle Federal Levee	5M to 20M	Q1 2007	HUBZONE

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Southeast Louisiana

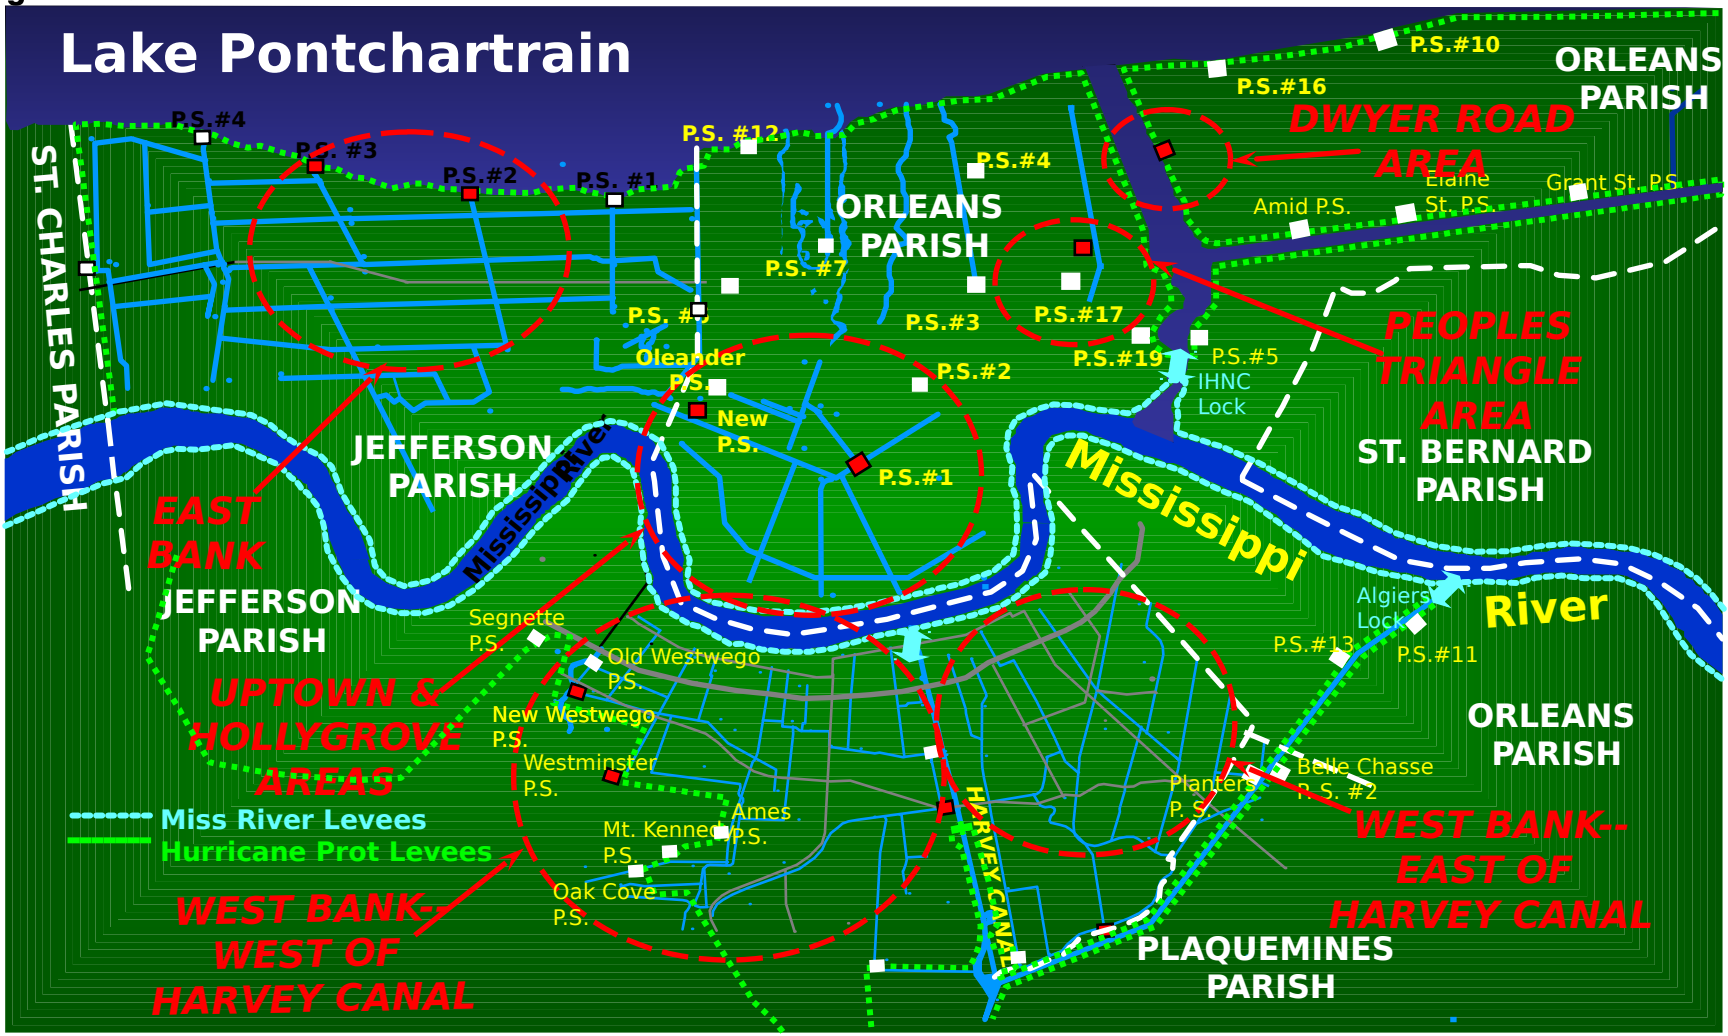

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Southeast Louisiana

- **Location:** The SELA project will cover portions of Jefferson Parish and Orleans Parish
- **Purpose:** Channel and pumping station improvements supporting the master drainage plan for flood protection.
- **Project Features:** 24 drainage canals and 6 pump stations
  - Orleans Parish
    - Major drainage lines
  - Jefferson Parish
    - Drainage canal improvements
    - Pump station improvements

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Southeast Louisiana Project Features

Project Code	Contract Name	Estimated Cost (in millions)	Expected Advertisement (Fiscal Quarter)	Acquistion Type
SELA-01	Soniat Canal - Veterans to Canal #3 & gap below Veterans	5M to 20M	Q4 2006	Unrestricted
SELA-01a	Soniat Canal - West Napoleon to Lynette	5M to 20M	Q1 2007	Unrestricted
SELA-02	Westwego PS Diesel Engine	0 to 5M	Q1 2007	8(a)
SELA-03	Westminster/Lincolnshire PS Backup Generators	0 to 5M	Q1 2007	8(a)
SELA-04	Elmwood Canal Bridge @ Kawanee	0 to 5M	Q4 2006	8(a)
SELA-04a	Elmwood Canal Bridge @ W. Esplanade	5M to 20M	Q1 2007	HUBZONE
SELA-05	Grand Cross Canal @ Lapalco	0 to 5M	Q1 2007	HUBZONE
SELA-06	Gardere Canal - Phase II	20M to 50M	Q4 2006	Unrestricted
SELA-07	Pump to River Disc. Tubes (Hickory Avenue Section)	0 to 5M	Q2 2007	TBD
SELA-11	Cousins Canal - Phase II	5M to 20M	Q1 2007	8(a)
SELA-18	Dwyer Road PS Intake Canal	20M to 50M	Q1 2007	Unrestricted
SELA-19	Florida Avenue - Phase 1	20M to 50M	Q1 2007	Unrestricted
SELA-20	Florida Avenue - Phase 2	50M To 100	Q1 2007	Unrestricted
SELA-25	Florida Avenue - Phase 3	20M to 50M	Q2 2007	Unrestricted

THIS IS NOT A SOLICITATION.
This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.

US Army Corps of Engineers®

Architect Engineer Service Contracts

Contract Description	Number of Contracts & Size of Firms	Base Year	Option Year 1	Option Year 2	Option Year 3	Option Year 4	Total Amount Per Contract
Geotechnical Studies and Investigations	1 (Unrestricted)	$40 M	$40 M	$20 M	NA	NA	$100 M
Construction Management Services	3-6 (8a, SB)	$20 M	$15 M	$10 M	$10 M	$10 M	$65 M
Design and Engineering During Construction	4-7 (SB)	$10 M	$10 M	$10 M	$10 M	$10 M	$50 M
Design, Engineering During Construction, Construction Management Services	1-2 (SB)	$30 M	$30 M	$30 M	$30 M	$30 M	$150 M
Design, Engineering During Construction, Construction Management Services	1-2 (SB)	$30 M	$30 M	$10 M	$10 M	$10 M	$90 M

THIS IS NOT A SOLICITATION.

This document is provided for information purposes only and is not intended as an obligation of the government to adhere to schedules or breakdown of items of work contained herein. Contract packages may vary in size and/or scope from the attached list. Solicitations dates may be revised from those included or may be omitted in its entirety.
